AQUAWATCH

TECHNICAL REPORT AQW-1

Preliminary Concept Study for the Satellite Segment of AquaWatch Australia

%UYE[EXGL 8IGLRMGEP 6ITSVX

4VIPMQMREV] 'SRGITX 7XY 7EXIPPMXI 7IKQIRX SJ %U %YWXVEPME

%YKYWX

012-!*,#-,#*(,133&!3-4#!.31,Б

Executive Brief

This report presents the findings of a preliminary concept study

™ The study has developed one mission concept in detail (mission concept A) and two alternatives, with lower performance and lower cost (mission concepts B and C).

™ Mission cost estimates for concept A indicate AUD 132M for one satellite, which includes, design, manufacture, integration and test, launch, operations and decommissioning.

™ Second and subsequent satellites of similar performance are expected to cost around AUD 47M including launch etc. Additional satellites will greatly improve the revisit time and overall benefits of the system.

™ There is the potential for cost and schedule savings by considering design reuse or economy of scale implementations with other Australian Earth observation proposals currently under development.

™ The economic, environmental, and societal benefits of operating AquaWatch are expected to be very large. Parallel, AquaWatch activities in Market Analysis and End User Consultation are being undertaken to quantify the expected impacts of AquaWatch.

™ We acknowledge the active participation and contributions to this study by domain experts from: UNSW Space, CSIRO, University of Queensland, Curtin University, SmartSat CRC, Australian National University, Geoscience Australia, Defence Science and Technology Group, and the Australian Space Agency (names listed in Appendix B).

Table of Contents

Executive Brief 1
Table of Contents 3
1 Executive summary 5
1.1 Introduction 5
1.2 Overview of AquaWatch 5
1.3 The

comprehensive data analytics platform, programs and data value-adding jobs that integrate prediction modelling, data analysis and environmental monitoring. This water quality and water health data will provide the necessary transparency required for water agencies and utilities that are the stewards of this critical resource.

Data scarcity is a critical issue facing effective water quality management due to lack of sovereign satellite assets, and limited number of in-situ observations across Australia - being logistically challenged and expensive to build, robust enough to survive extreme weather and climatic conditions, and historically have been built to measure water quantity.

AquaWatch will aim to compliment and contribute to existing national water resource accounting programs, and provide precise, real-time, decision- U H D G \ L Q I R U P D W L R Q R Q W K H T X D O L W \ R I Z D W H reservoirs, and coastal environments, and its variations over time and space, including degraded water quality, ecological integrity and freshwater resiliency in a changing climate.

This data will provide early warning of water quality threats, predicting and mitigating the effect of local and global environmental events (bushfires, storms, harmful algal blooms) and industrial stressors (pollutants, infrastructure assessment, management & remediation) and monitoring and analysing the freshwater and marine eco-systems (supporting sustainable growth in primary industries) to deliver tangible widespread societal, economic and environmental benefits to Australians.

space segment including Earth Observation satellites with hyperspectral cameras, and the ground segment which includes stations for data downlink and Telemetry, Track & Command (TT&C).

The results of this work will inform the Australian Government Satellite Earth Observation from Space Technology Roadmap being developed by the ASA, the BoM, CSIRO, the Department of Defence, and GA in close partnership with the Australian Earth observation community.

1.5 Applicable Documents

1. CEOS (2018): Dekker, A.G & Pinnel, N. (Eds) Feasibility Study for an Aquatic Ecosystem Earth Observing System. CEOS Report, CSIRO, Canberra, Australia

2. Dekker, A.G. and MacLeod, A. (2021) AquaWatch Australia ±Phase 0 End-user Consultation.

2 Table of Figures

Figure 1: System Engineering V-Model applied to AquaWatchPhase-0 10

Figure 2: Methodology for development of satellite requirements (CEOS report = CEOS (2018)). 12

Figure 3: Launch Price per Kilogram ±a comparison 33

Figure 4: Highest impact on the outcome of current Phase0_survey results 47

Figure 5: Technology pathfinders that aim to de-risk different sub-systems towards a fully operational AquaWatch Australia system 55

3 Table of Tables

Table 1: NASA definition of space mission Pre-Phase A (Phase 0) 11
Table 2: Overview of second AquaWatch CDF study 12
Table 3: AquaWatch end user requirements for hyperspectral imaging 15
Table 4: AquaWatch end user requirements for thermal imaging 16
Table 5: AquaWatch end user requirements for water quantity 17
Table 6: AquaWatch Satellite Requirements ±Baseline for CDF study 19
Table 7: Mission Options Table 23
Table 8: Mission Overview 26
Table 9: AquaWatch Payload Compared to Closest Analogues 28
Table 10: AquaWatch Orbital Considerations Compared to Closest Analogues 29
Table 11: AquaWatch Optical Path Specifications Compared to Closest Analogues 30
Table 12: AquaWatch Camera Architecture Compared to Closest Analogues 30
Table 13: Camera Design Parameter Definitions 31
Table 14: Preliminary SNR Results 31
Table 15: Satellite Weight Analysis 31
Table 16 Cost estimation method 2 34
Table 17: NRE vs RE Costs 35
Table 18: Risk Table 37
Table 19: Component TRL Analysis 41
Table 20: Services TRL Analysis 44
Table 21: Abbreviations and acronyms 50
Table 22: List of People Involved in the Study 53
Table 23: ROM cost estimate for a single CyanoSat mission 56
Table 24: ROM cost estimate for a single CHICOSat mission 57

5 User Needs and Technical Requirements

Establishing the technical requirements of the satellite and sensor networks that will comprise AquaWatch requires two key components: first, an understanding of end user needs, water management authorities, aquaculture industry, and many other stakeholders; and second, a thorough understanding of the science that links remote sensing data to actionable water quality information.

5.1 Inputs to the CDF

In this section we outline our appro5.1

Table 5: AquaWatch end user requirements/goals for water quantity

Parameter/Requirement	Breakthrough	Target
Ground resolution	30 m	10 m
Orbital revisit time, all water bodies in Australia	5 Days	

The primary observable region of interest is also important in determining the mission architecture. For example, the , W D HPRISMA ¶mission is a single spacecraft with a published body pointing capability of ± 15 degrees and a primary region of access bounded by ± 70 degrees latitude since Europe and the Mediterranean are of most interest[3]. 7 K H (X U R SeHtDeQ2 ¶µ

Minimum radiances to be observed, L_{min}	412 nm: 30 490 nm: 16 560 nm: 10 665 nm: 5 778 nm: 2 865 nm: 1	W- m^{-2} mm^{-1} sr^{-1}	TBR
Typical radiances to be observed, L_{typ}	412 nm: 80 490 nm: 55 560 nm: 40 665 nm: 20 778 nm: 10 865 nm: 5	W -m^{-2}	

Striping and detector to detector response variations	TBD	TBD		Minimise during calibration

The resolution requirements for spatial, spectral and radiometric performance would be refined in a future Phase A study. The values presented here have been informed by and would follow accepted user-community definitions for these key system performance metrics[7]. The radiance levels were provided by Curtin University during the study.

[7] https://esto.nasa.gov/files/SLIT2015/RMAKeyParameters.pdf

the imager and onboard processing to estimate water quality parameters, to reliably detect water bodies and clouds is validated by comparison with in-situ or other referenced remote sensors.

3. Water Quality Monitoring (normal operations). The satellite continuously images most of the daytime side of the Earth from Sun-synchronous (polar) orbit, potentially excluding very high latitude polar regions. Onboard data processing (described below) reduces the data and reformats it such that it can be used to deliver water quality estimation.

With regards to control and monitoring, the satellite would be controlled by two methods:

1. Routine operations - Mapping and automated water body imaging.
2. Tasked operations ±Scheduled observations of targets of opportunity.

The satellite would be controlled from a mission operations centre (MOC) which would be responsible for:

- Overall control and monitoring.
- Logging the

Where the signal S has the following functional dependencies on the system parameters.

Table 13: Camera Design Parameter Definitions

Design parameter	Description	Signal dependency
Lref	At aperture radiance	Lref
p	Pixel width	p^2
f	Focal length	$1/f^2$
D	Telescope aperture diameter	D^2
Q	Œf / p	Q^2
t_{int}	Integration time	t_{int}
K O	Spectral quantum efficiency	**K O**

7.4 Launch Segment

We anticipate that AquaWatch would be the primary customer for a launch to inject the AquaWatch spacecraft into a desired orbit. In this study we considered launchers that have a capacity above the required launch mass with some margin. For example, the. Falcon 9 was excluded since the margin is so large. The 5 R F N H W / D E ¶ V (O H F W U R Q O D X Q F K Y H K L F O H V

Considering the current market offerings as shown in Figure 3, we have used the example of a Virgin LauncherOne for use in initial planning based on its:

- payload capacity for SSO is just above the required value for AquaWatch.
- specific cost close to an ³ D Y H U D J H ´ H [S H Q V L Y H

Figure 3: Launch Price per Kilogram ±a comparison

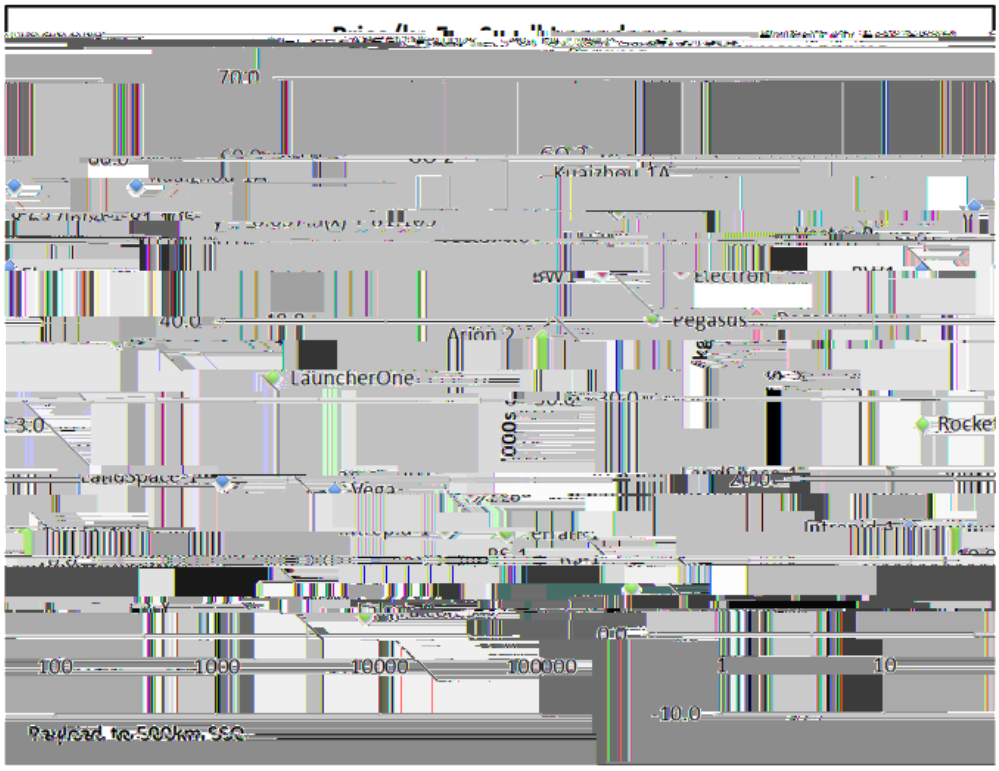

Figure supplied by Andrew Barton, Research Program Manager, Smartsat CRC. The Virgin LauncherOne would lead to launch costs of ~USD 36K/kg. It is worth noting that these figures are reasonably conservative as the market becomes more competitive and launch costs are decreasing with time.

AUD 106M. This compares reasonably well with the first method but is also a reasonable indicator of the error bars on this cost analysis.

8.3 Non-Recurring Engineering vs Recurring Engineering Costs

The example of a bottom-up cost estimate in Table 17 (created post-CDF) is presented to

	Negligible	Significant	Major	Critical	Catastrophic
Medium Likelihood		Changes to CSIRO or SmartSat CRC priorities force replanning. Unavailability of required test facilities. Short schedule leads to technical failure. Contractual disputes over procured goods and services. Product warranty issues. Underestimate of effort/time for spectrum licensing. Mechanical failure during AIT	Uptake of AquaWatch data products. Incomplete or inadequate testing. Products/subsystems do not meet performance requirements. Overseas supplier management and procurement challenges. Limited/no value to international partners (e.g. Sentinel) Restrictions to travel or shipping. Delays in delivery of major subsystems for system integration Schedule runs overtime for the development of software. Pointing inaccuracy Payload specification leads to unavailable component choices. Final product does not (fully) meet end user needs. Cost Overruns Cleanliness requirements too demanding for existing facilities Commissioning of the spacecraft takes longer than expected	System has a very high operating cost Scope / requirements creep Loss of stakeholder/sponsor support. ADCS electronics or software failure leading to loss of spacecraft attitude knowledge/control	

™ The ability to source products and services globally, where there is much more choice and competition, and where TRLs for the required technology is also improving.

™ The ability to identify and perform targeted R&D through the AquaWatch precursor program.

™ The ability to collaborate and push technology, particularly where there is potential design reuse or commonality with parallel missions in Australia.

Element	Subsystem	Item	Performance	

Element	Subsystem	Item	Performance	Option	Current TRL	Expected TRL8	

- Distraction from operational mission
- Cost increase of whole programme
- Probity and possible conflict of interest due to working with pathfinder contractor.

9.2.2 Mission options

There was a discussion around Pathfinders that would address most of these objectives within the CDF study. The following rating in Figure 4 was given by study participants to applicable, existing or planned pathfinder opportunities:

Figure 4: Highest impact on the outcome of current Phase0_survey results

The CyanoSat and CHICOSat concepts have emerged throughout Phase 0, as our general understanding of the AquaWatch mission and its needs has emerged. They are envisaged as precursor CubeSats designed and built under the AquaWatch mission to demonstrate the system, prove the technology (R&D, TRLs, risk mitigation), resolve outstanding trade-offs, support iterative approaches to Software Development and provide representative data to end-users. This CDF study not only supported the pursuit of these precursors, but it also informs their scoping.

- 7 K H & \ D Q R 6 D W ´ S Dwould be designed specifically for detection of cyanobacteria and harmful algal blooms. This satellite would utilise a multi-spectral camera and be a relatively simple design, with lower specifications than the planned AquaWatch satellites. This would aid in optimising the AquaWatch satellite design by confirming the model-based systems engineering approach that that is applied to the dynamic range of AquaWatch satellites. The CyanoSat would additionally demonstrate a vertically integrated and operational system, including downlink, data processing and data archiving. CyanoSat would provide valuable & representative data to end-users and have an immediate impact on management of water resources in Australia. This project would be similar in size and scope to the SASAT-1 mission[13].

- 7 K H H&O 6 D W ´ S D Would be designed specifically to provide flight heritage to a representative Hyperspectral Imager. In this case we would aim to use

Appendix A: Abbreviations and Acronyms

Table 21: Abbreviations and acronyms

Abbreviation	Description / meaning

Abbreviation	Description / meaning
FoV	

Appendix B: Study Participants

The list of experts involved in or consulted as part of the study is presented in the table below.

Table 22: List of People Involved in the Study

Organisation	Person	Role / contacted for
ANU / AITC	Rob Sharp	Optical payload specialist
ASA	Arvind Ramana	Earth Observation, Space Technology & Advanced Communications
CSIRO	Alex Held Adam Macleod Stephen Gensemer Tim Malthus Nick Carter Kimal Hiralall	AquaWatch Mission
Geoscience Australia	David Hudson Medhavy Thankappan	SCR programme
UNSW Canberra Space Australian National Concurrent Design Facility	Denis Naughton Lena Meyer Igor Dimitrijevic Anthony Kremor Sam Boland Jan-Christian Meyer Andrin Tomaschett Damith Wickramasinghe	Mission design and domain expertise
SmartSat CRC	Andrew Barton Allison Kealy	Research programme 2 coordination
University of Queensland	Stuart Phinn	Earth observation remote sensing expert
SatDek	Arnold Dekker	Inland water remote sensing expert
Curtin University	David Antoine	Ocean water remote sensing expert

Appendix C: Australian Hyperspectral Instrument Pathfinder

An Australian built hyperspectral sensor for a smallsat requires considerable research and development investment. The not inconsiderable associated cost and schedule risk is best managed through a scaled development program enabled through a series of pathfinder missions to demonstrate key scientific, technological and operational components.

At the highest level, a hyperspectral sensor comprises a detector, optical imaging system (telescope), command and control systems, and satellite support capabilities. Based on assessments of the Australian space sector the telescope appears within the capability of several Australian integration vendors today (optical components will still require overseas fabrication but are widely available from multiple sources).

There are a range of focal plane DUUD\ GHWHFWRU VROXWLRQV IRU WKLV W\SH RI YLVLRQ´ VROXWLRQV DevelopmentXUHs provide only basic performance. There are well established international vendors (e.g. Teledyne, Sofradir), but no Australian commercial vendor (although significant local development for infrared array technology has emerged in recent years). Inexpensive COTS camera systems are likely well suited to early-stage pathfinder developments, however larger generation systems addressing the stated goals of the AquaWatch program will require higher performance devices. These higher-grade solutions typically also require bespoke detector control electronics. The inclusion of on-board processing and in-flight Artificial Intelligence (AI) will likely present data latency challenges requiring bespoke control hardware/firmware to be developed and flight tested via a staged pathfinder program.

A staged pathfinder development program is well supported by the Australian local satellite platform and operational support industry ecosystems. A range of current generation platforms would allow agile and inexpensive flight verification of sub-components and first-generation sensor systems, while active symbiotic developm

- Provide hyperspectral capabilities, allowing tuneable post processing for multiple end user applications.

The specific technological challenges being explored by the CyanoSat and CHICOSat pathfinders on a pathway to a VNIR pan-hyperspectral system that has simple detector cooling requirements, broad user appeal with a wide range of cross calibration data opportunities are as follows:

- x TDI-like operations (not reliant on forward motion compensation due to CubeSat ADCS performance limitations);
- x Modest ground resolution (GSD ~ 20-
