© The University of New South Wales, 2021.
Published by UNSW Canberra Space, March 2021.

Australian National
Concurrent Design Facility

Development of a Satellite Cross-Calibration

10.4 Integration and system-level testing 29
10.4.1 Description 29
10.4.2 Procurement approach aspects 29
10.4.3 Implementation options 29
10.4.4 Element cost estimate 29
10.5 Payload calibration 30
10.5.1 Description 30
10.5.2 Procurement approach aspects 30
10.5.3 Implementation options 30
10.5.4 Element cost estimate 30
10.6 Environmental qualification and launch 31
10.6.1 Description 31
10.6.2 Procurement approach aspects 32
10.6.3 Implementation options 32
10.6.4 Element cost estimate 32
10.7 Processing pipeline and data distribution 33
10.7.1 Description 33
10.7.2 Procurement approach aspects 33
10.7.3 Implementation options 33

3 Table of Figures

Figure 1: SCR programme overview (for detailed description refer to section 9.3) 12

Figure 2: SCR mission architecture overview 17

Figure 3: SCR mission specification hierarchy 37

Figure 4: Circular-to-circular orbit manoeuvre delta-V requirement as function of initial orbit altitude and change in altitude 53

Figure 5: Propellant mass fraction depending on delta-V and specific impulse of propulsion subsystem 53

Figure 6: Thrust duration as function of delta-V for a 1.8mN thruster on a 50kg satellite 54

Figure 7: SCR lifecycle radiometric calibration approach overview 57

Figure 8

Four technological elements have been identified as opportunities for immediate de-risking and local manufacturing capability increase:

- A hyperspectral instrument meeting the SCR observation and size requirements
- An on-board calibration subsystem for hyperspectral small satellites
- A payload data handling subsystem capable of handling data rates of at least 200Mbps and of simultaneously writing to and reading from mass memory

8 Background

6DWHOOLWH (DUWK REVHUYDWLRQV FRQWULEXWH through U E applications in industries as diverse as weather prediction, agricultural production, climate monitoring, climate adaptation, mining and extractive technologies, financial services, infrastructure development, environmental monitoring and disaster management. Government agencies who depend on such services include Geoscience Australia, CSIRO, Bureau of 0HWHRURORJ\ DQG YDULRXV 'HIHQFH DJHQFLHV 7KH 86¶ /DQ

9 Mission overview and background

This chapter provides a high-level overview of the mission, its scientific, policy and industry benefits and how it relates to other existing or planned international Earth observation satellite missions.

9.1 Mission concept

The high-level mission objective is as follows:

> The SCR mission programme would collect coincident spectral radiometer data between cooperative optical satellite missions for the purpose of enabling cross-calibration in a continuous, worldwide service.

Each of the SCR satellites in the programme would be a small satellite (<100kg) operating a hyperspectral sensor in a low Earth orbit (LEO). The orbit would be selected to enable coincident observation with both highly-calibrated optical missions (e.g. Landsat 8, Sentinel 2) and targeted cooperative missions (e.g. Planet Doves). It would thus yb Q e n 0 0 (e)]TJ ETo Q on.

9.2 Benefits

The SCR mission would provide both scientific, policy and industry benefits. They are outlined in the following sections.

9.2.1 Scientific benefits

between potential and actual use of Earth observation in this sector which operates over more than

9.5 Related missions

This section provides an overview of current and planned

9.5.6 Australia as a global test track for Earth observation calibration and validation

%XLOGLQJ RQ $XVWUDOLD¶V JOREDO UHSXWDWLRQ for Radiometric Calibration and Validation there are active discussions across Australia about a proposal to codify this position and developing Australia as the global satellite test track for Earth observation satellite calibration and validation. This strategy has three components:

1. A comprehensive, operational network of calibration and validation facilities across Australia
2. A suite of tools to enable global satellite operators to use the infrastructure
3. A series of Satellite Cross-Calibration Radiometers to provide improved accuracy and consistency between optical satellites (this study)

9.6 Relationship between SCR and related missions

The CLARREO mission was recommended in the 2007 Decadal Survey to deliver needed climate model and sensor inter-calibration improvements. Although CLARREO was discontinued the CLARREO Pathfinder (PF) mission was begun in 2016 to raise the TRL for the radiometer subsystems0f6039695 (he)1edT /TT1 11.0T1 11.04 Tt-3.995 (red)2.998 ( )275 (5 (e)12.998 (m)-2.998 (ed)2.99

10 Mission elements

This chapter provides a high-level overview of all mission elements (see section 9.1) and compares differences in procurement options to come to an estimate of ROM cost for each of them

In parallel to the bottom-up cost estimation approach described above, the CoBRA parametric cost model[31] has been utilized to provide a sanity check of the mission cost. Details of the model are provided in section 11.6.5. This approach yields a total mission cost of AUD83 M (FY2020) when adjusted for inflation and currency conversion with an error of ±25%. Due to the underlying cost data making up this model, its transferability to the modern Australian satellite manufacturing context is questionable. In a calibration exercise W K H P R S R V H G cost estimate has been translated to the Australian context resulting in an adjusted cost of between AUD17 M to AUD33 M. This excellently confirms the bottom-up figures derived here. Section 11.6.5.1 provides further details on the limitations and calibration of the CoBRA cost model.

Considering these findings leads to the conclusion that the estimated ROM mission cost provides a credible assessment of the actual SCR mission cost at this early stage of design. It is recommended to perform a refinement of this cost assessment as part of the next step in the mission development process once the technical concept is properly defined.

The following sections provide for each of the mission elements listed in the bottom-up cost estimation:

- A concise description of what is included in each element
- A brief discussion on different procurement options (i.e. make vs. buy considerations). These are kept generic, ignoring any specific vendors or manufacturers
- An assessment of specific implementation options, listing potential vendors
- $Q H V W L P D W H R I W K H H O H P H Q W ¶ V 5 2 0 F R V W D Q G X Q F H U W D L

[31]

10.2 Payload

10.2.1 Description

The SCR is envisioned to be a hyperspectral imaging spectrometer that provides the performance capability needed to meet the mission requirements which were refined in the study.

The SCR instrument would include a telescope and focal plane arrays to cover a spectral range from 400-2400 nm with a 10 nm band centre wavelength spacing. The instrument would provide SNR between 100 ±300 depending on the spectral band ranges. In addition, the SCR platform would include a means to accurately maintain radiometric calibration over the mission life. This could include a passive solar calibration unit or an LED based calibrator.

10.2.2 Procurement approach aspects

Several options were considered for a SCR Pathfinder (PF) and SCR Full Operational Capacity mission (FOC). A review of the currently available instruments and the descriptions of instruments being designed for use as the SCR was conducted. The SCR mission requirement for radiometric accuracy places demanding instrument requa 595.32 841.[1.62 Td [21t.996 (on)2.9.998 (m)-2 (i)5 (ng)bo998 (r

10.3.3 Implementation options

10.6 Environmental qualifica

10.7 Processing pipeline and data distribution

10.7.1 Description

The data processor pipeline consists of one G D W D D V V H P E OW F SK LD QV JH four processing stages (L0, L1, L2, L3). The stitcher would be provided by GA and would interface the mission archive to the L1 processor. A further description can be found in section 11.5.3.

A focus on secure software development should be made to ensure the risk of any cyberattack is sufficiently mitigated. See section

11 Analyses

This chapter provides detailed analyses performed during the study or evidence supporting high level information provided in the previous chapters of this report. The following sections follow a loose top-down order, but should be considered as independent chapters to be read in conjunction with the appropriate sections further up in this report.

11.1 Systems engineering analyses

11.1.1 Requirements analysis

A core part of the CDF activity consisted in a detailed derivation of mission requirements from the F X V W R P H U. ¶V Q H H G V This section outlines the various levels of requirements identified in this process.

The following sets of requirement specifications have been defined at this stage:

- Mission objectives as stated by the customer
- Observation specification as derived from the mission objectives and technical analyses into the required performance
- Blackbox platform requirements as derived from the observation specification to inform a small RFI campaign among satellite bus providers
- Pathfinder mission descope

11.1.1.4

11.1.2 Trade-offs

At this early stage of the SCR mission design, several key trade-offs have been identified. Not all of them have been assessed at this stage.

- Orbit selection (linked to reference mission selection)
- Instrument design / COTS option
- Propulsion
- Number of star trackers
- Spacecraft mass range / form factor
- Payload data downlink RF band
- Spacecraft antenna concept
- Ground station locations and size
- Test model philosophy
- MOC operation staffing
- Include lateral off-nadir pointing in ConOps (as goal only)

The first 10 of the above trade-offs have been considered together for the SCR pathfinder mission. I.e. three combinations of the individual options have been created to identify a baseline system concept for the pathfinder mission. This is described in more detailed in the following section.

11.1.2.1 Pathfinder system concept trade-off

11.1.3 Risk assessment

Risk item	Applicable to	Likelihood	Impact	Mitigation actions
Space craft is dead-on-arrival	All	Minimum	Catastrophic	Rigorous, appropriate and relevant test campaign with focus on LEOP. Pathfinder timeline with suitable time to apply lessons-learnt to FOC
Collision with other A-train spacecraft	All	Minimum	Catastrophic	

Risk item	Type	Likeli - hood	Impact	Comment
Space segment not ready for launch on schedule	Programmatic	High	Significant	
Spec doesn't demonstrate transfer cross-calibration	Technical	Medium	Major	
Launch delay due to launch provider	Programmatic	Medium	Major	Overseas only
Pathfinder failure impacting FOC mission	Programmatic	Medium	Major	
Environmental AIT facility readiness/capacity	Programmatic	Medium	Major	AUS-made only
Procurement flexibility to account				

Risk item	Type	Likeli - hood	Impact	Comment
HSI imager not meeting operational lifetime	Technical	Low	Major	
Cyber attack on ground segment (GS and processing chain)	Programmatic	Low	Major	mitigation actions identified

The table below lists risk items of low magnitude as identified in the study. Again, many of them will benefit from mitigation actions identified for high-risk items above.

Table 12: Low risk items identified

Risk item

11.2 Mission operations

11.2.1 Concept of operations

The SCR mission Concept of Operations (ConOps) relies on two operational modes:

- The default mode is to perform imaging during predefined intervals of coincident observations.
- A secondary mode consists in the continuous imaging of all land cover.

In the default mode, the opportunities for coincident observations are computed on ground based on the ephemerides of all cooperative missions. The results of this computation are then used to define W K H V D W H O O L W H V L P D J L Q J V F K H G X O H V. In a First Order, this operational mode would fulfill all immediate needs for image acquisition while keeping the data volume to downlink to ground to a minimum.

The second mode would allow to store image data in a ground archive for future use. This can serve use cases that are currently not identified but may become of interest in the future. Since this mode leads to a significant increase in the payload data budget, it shall only be implemented to the extent that it does not drive the system design.

With either of the two operational modes it shall be possible to perform imaging while downlinking payload data to a ground station. This would define a dedicated spacecraft mode with potentially challenging implications for the power budget, on-board payload data handling and antenna design.

Imaging operations would be interrupted on a regular basis to perform instrument calibration. This

that are received, including housekeep telemetry, configuration data, payload data, and spacecraft log files;
- x methods to set warning limits for telemetry fields so that operators can be immediately notified of non-nominal spacecraft health;
- x software tools for visualisation and trending of spacecraft telemetry;
- x methods to export and share telemetry and payload data in accessible formats.

Significant up-front development is required for the MOC prior to the first SCR series pathfinder, after which only updates and maintenance are required for continued reliability and compatibility with later missions. An initial investment in operations development is expected to pay off with reduced operational costs after launch and greater mission outcomes. The MOC would be used for on-orbit operations, operator training, and as discussed in section 10.8, system level testing before and after launch.

Table 13 lists the elements of the MOC and their estimated costs. The assumptions made in this cost estimate are:

- x the software infrastructure would be developed from the ground up, or substantial modification would

component during the mission,0 G



Figure 4: Circular-to-circular orbit manoeuvre delta-V requirement as function of initial orbit altitude and change in altitude

The required mission delta-V in combination with the selected propulsion technology would GHWHUPLQH WKH PDVV IUDFWLRQ RI WKH SURSHOODQW UHOD is plotted exemplarily for a 50kg spacecraft in Figure 5. The range of specific impulse (Isp) values included in the graph represents the range as achievable by cold gas (<100s) over chemical (150s ±350s) to electrical (>1000s) propulsion subsystems. To continue the above example: For a 100m/s mission, a cold gas system would require ~10% (=5kg) of propellant, while an electrical system would need <1% (=0.5kg).

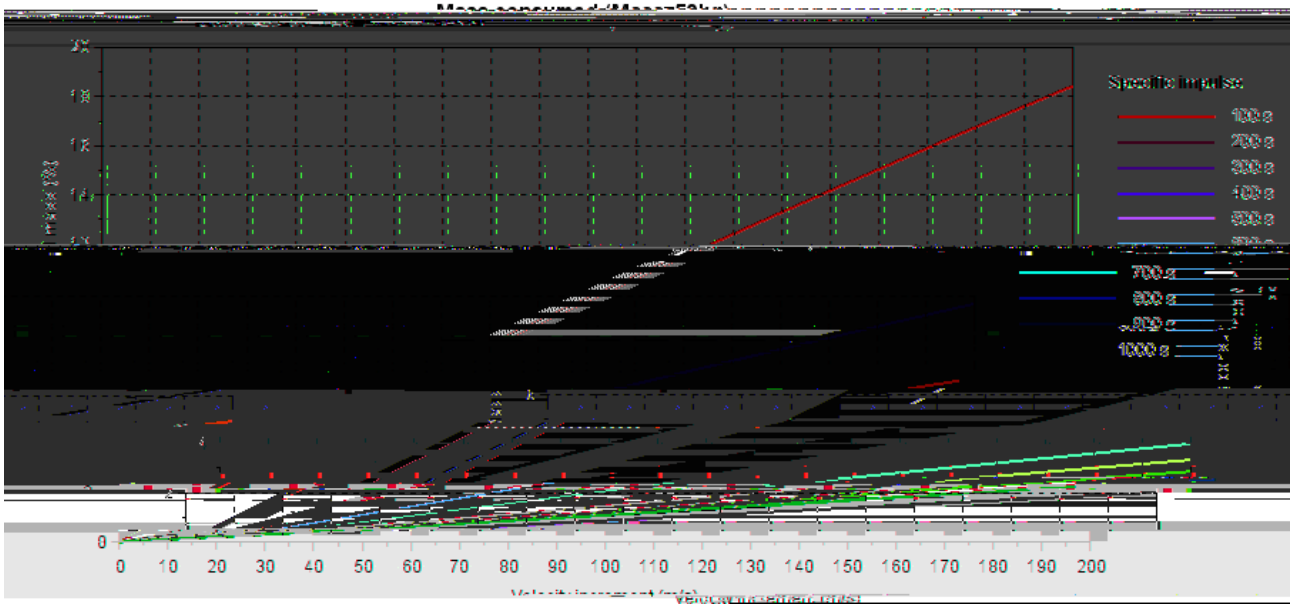

Figure 5: Propellant mass fraction depending on delta-V and specific impulse of propulsion subsystem

While fuel efficiency increases for higher Isp propulsion subsystems, thrust decreases. Typical thrust levels for Hall-effect thrusters (Isp ~1000s) are in the order of a few mN. This leads to the need of a substantial period of time for thrusting to achieve a certain orbit change. Continuing the above example, performing a manoeuvre of 100m/s using a thruster with 1.8mN of thrust requires ~3E6s or 35 days of continuous thrusting as plotted in Figure 6. This does not consider the fact that typically

11.3 Payload assessment

11.3.1

11.3.2 Payload calibration

The SCR mission objectives for calibration would be the same as for example CLARREO Pathfinder[58] or TRUTHS where SCR would conduct on-orbit SI-traceable calibration[59] of spectral scene radiance/reflectance at an improved accuracy over other sensors and to use that improved calibration of other sensors such as Landsat, Sentinel-2 and others.

Accuracy and stability requirements for satellite measurements in the reflected solar and SWIR bands are necessarily stringent for climate and weather applications and satellite sensor cross-calibration. Calibration requirements that are traceable to SI standards would be imposed such that tools for characterizing the geometric, radiometric and spectral performance of SCR and for generating correction parameters to be applied to the datasets can be adequately developed. As such, this requires exacting pre

11.3.2.2 In-Flight Calibration

The goal of in-

maintain their stability. Despite these design practice implementations, the lamps themselves can change in colour temperature over time and diffuser material scattering properties can change due to the harsh space environment.

In addition to radiometric calibration operations, the acquisition of designated terrestrial targets would be used to assess the SCR in-flight measurement of spatial resolution parameters, including ground sample distance, far field response, edge response and modulation transfer function as well as geo-reference accuracy. These acquisitions would be part of normal calibration operations over the mission life[61].

11.3.3 Payload options

Several options were considered for a SCR PF and SCR FOC mission. A review of the currently available off the shelf instruments and those being designed for use to support the Sustainable Landsat Imaging program was conducted. The results are summarised in Table 15 which provides a checklist of performance capability against the preliminary requirements (Table 5). Green ticks indicate compliance with the observation requirements, red font indicates non-compliance. At this stage, no distinction is made between partial and non-compliance. For example, while the ANU VIS and Eartheye sensors provide a SNR >100 across all bands, they do not achieve the expected required SNR closer to 300 in some critical bands. This has not been analysed in detail, but should be done in a future design study.

Ball Aerospace in partnership with NASA is developing systems such as the REMI-AB and CHPS-AB instruments. These have recently completed airborne testing flights[62]. The CHPS sensor is considered to be the currently best available candidate for the SCR FOC.

Another possibility for use on the SCR PF could be the Micro-HyperSpec from Headwall Photonics. This would be investigated in the next phase of the project along with the HyperScout2 for inclusion on a SCR PF mission.

Table 15

11.3.4 Payload data handling

11.4 Satellite platform subsystems

11.4.1

11.4.3.1 Platform software

The

The resulting daily contact times are provided in

11.5.2 Ground segment cost assessment

The ground segment contracted cost is estimated at AUD0.4 M based on an FTE-year costed at AUD200k. Details are provided in Table 19.

Table 19: Ground segment cost estimation details

Aspec t	FTE	Duration [months]	FTE-months
Scoping / design	1	3	3
Development			

11.5.3

Manu-facturer	Platform	Cost figure	No of sat ¶	ROM cost per satellite	Reference	Comments
	S-Class	USD 12.8M	1	USD12.8M	Space News website[68]	Tetra-3 mission for USAF.
	S-Class	USD 1.2M	1	USD1.2M	Space News website[69]	Company advertised cost for platform.
Berlin Space Technology	Kent Ridge	EUR 5M		EUR5M	Handelsblatt[70]	LEOS-50 platform Includes launch costs but this is not

Table 26: TRL and expected development for SCR-required technologies

Element	Sub-system	Item	Performance	Option	Current TRL	Expected TRL development

11.6.4.2 Team maturity and experience

11.6.5 Parametric cost estimation

In order to support the bottom-up costing of the SCR mission, a second approach was used to derive an estimate of the mission cost. In this approach, a parametric cost model developed by the Aerospace Corporation based on the Complexity-Based Risk Assessment (CoBRA) tool

Abbreviation	Description / meaning
S/C	Spacecraft
SCR	Satellite Cross-Calibration Radiometer
SM	Structure model
SNR	Signal-to-noise ration
SSO	Sun-synchronous orbit
STAC	SpatioTemporal Asset Catalogs

14 Appendix A: Study participants

The list of experts involved in or consulted as part of the study is presented in the table below.

Table 31: List of personnel involved in the study

Organisation	Person	Role / contacted for
AGO	Mathew Withheld	Study participant link to defence (DEF799)
ANU / AITC	Rob Sharp	Optical payload specialist
Australian Space Agency	Aude Vignelles	Programmatic guidance
	Reece Biddiscombe Arvind Ramana	
